

Homework 3: Project Schedule and Budget

Team 09

ADA University

Fall 2025 IT Project Management (INFT - 3609 - 10862)

Araz Yusubov

Table of Contents

1. Updates in Project Charter

1.1.Scope and Structure

1.2.Dates and Schedule

1.3.Budget

2. Project Schedule

2.1.Explanation of Schedule Development

2.2.WBS

3. Project Budget

3.1. Explanation of Budget Table

3.2. Resource Sheet

3.3. Uzbekistan Calendar

3.4. Project Budget Table

4. Gantt Chart

4.1.Explanation of Gantt Chart and Critical Path

4.2.Visualization

Individual Contribution Table

References

1. Updates in Project Charter

1.1. Scope and Structure

In the previous project charter, project scope was described as a set of high-level milestones including authorization and competition dates. However, in Microsoft Project those milestones are listed inside a Work Breakdown Structure with separate tasks and subtasks by adding detailed work.

First, the milestones mentioned in the project charter as “finalize the project charter and establish the project team”, “conduct the stakeholder kick-off meeting” and “approve the budget and complete financial planning” were placed under a dedicated stream of “Project Management” separated as initiation, planning, monitoring & control, and planning.

Second, for venue related milestones as “conduct the venue selection process”, the WBS has identified tasks as inspections, contracting, and installation. Similarly, a complete milestone for “complete IT platform development” developed as a pipeline with clear tasks as testing phases, deployment, and validation.

Third, in the project charter, accommodation, transport and catering services weren’t clearly defined which shouldn’t be overlooked. Our current project schedule clearly mentions those milestones converting them into dedicated tasks. Furthermore, branding and sponsorship milestones are improved into separable tasks including promotional materials, and media partner agreements. In addition, human resources were added as a separate milestone for covering volunteer trainings and recruitment.

Finally, security and medical services weren't considered in the previous project charter, however, it is an important milestone. It has developed with tasks including emergency readiness and daily medical monitoring.

1.2. Dates and Schedule

The milestone dates mentioned in the project charter are kept, however, different start and finish dates assigned to subtasks for making the process more precise. Since the dates are too general in the project charter, we needed to do some adjustments in some tasks so that each task fits logically into the overall time interval.

For example, according to the charter, "infrastructure setup" has completed in December 2025, however, we decided to consider it during September 2025 and December 2025. Those improvements helped us to reflect the real effort. An important improvement that was made is about Winter meeting conducted in Tashkent in January 2026. It is an important point as it is an essential dated deliverable with a preparation period.

Contest days 1 and 2 clearly defined inside the competition week mentioned as in the project charter. Finally, although the project charter end date is mentioned as September 2026, we had to extend it to October 2026 considering closing and reporting.

1.3. Budget

In the project charter, the budget is mentioned around 2.5 million dollars divided by categories as percentages (catering 18%, transport 8%, accomodation14%, venue/infrastructure 12%, IT 15%, promotion 6%, contingency 6%). In Microsoft Project, the budget is calculated using bottom-up estimation. As each task has an assigned resource that have hourly rates in resource sheet, Microsoft Project calculates

the cost at task level and apply the summary to WBS items. The current budget for each milestone is:

- Project Management: \$76 448
- Venue & Infrastructure: \$952 488
- IT Systems & Contest Platform: \$382 808
- Branding, Media & Sponsors: \$251 056
- Human Resources: \$125 840
- Contest Operations: \$908 312
- Security & Medical Services: \$120 376

The total makes \$2 817 328 which is higher than the planned charter estimate. However, the difference is explainable as Microsoft Project calculated the cost in a detailed way. Additionally, the charter mentioned 10% margin of error for success criteria, therefore our current budget can be justified.

2. Project Schedule

2.1. Explanation of Schedule Development

The project schedule formed converting the milestones mentioned in the project charter into a Work Breakdown Structure. Then, using logical dependencies tasks placed in a sequential order. Mainly, predecessor IDs have been used in Microsoft Project as dependencies. For example, contracting should be done before setup, development before testing and so on. For predecessors, finish-to-start relationships are used by default. Furthermore, there are some fixed dates for some specified activities as Winter Meeting that reflect real-world constraints.

Project Management covers the coordination work required to host IOI 2026 as a project.

It has 4 tasks initiation, planning, monitoring & control, and closing that reflects a project lifecycle.

In Project Initiation, the work begins with formal approval for starting the project mentioned as “Obtain authorization”, then “Confirm charter” for making sure about the validation of the charter before planning the upcoming steps. The initiation ends with forming project team to confirm the core structure of management and assign responsibilities.

Project Planning provides the direction for execution the output, in our case the event. It begins with “Stakeholder kick-off meeting” for discussing project goals and expectations. Then “Approve budget” task ensures that the budget and other financial issues have been confirmed beforehand. Planning includes “Risk Management plan” because this large event may have considerable risks about venue, IT reliability, safety and so on. Lastly, planning includes preparation and conduct of Winter meeting. As it is a deliverable and has a fixed date, it must be reviewed in terms of major event related decisions.

Project Monitoring & Control is very important as project timeline is long and have multiple tasks running parallel. It includes “Weekly status meetings” for having constant reporting between teams. Then “Scope & timeline monitoring” for preventing any schedule changes and ensuring dependencies. Also, “Change & quality control” is included to handle any changes and ensure standards about quality are followed for risky tasks as contest systems and competition week operations.

Since the project doesn’t end when contest ends, a formal Project Closing is needed. It is done through “Final evaluation” to measure results with objectives, “lessons learned” to see improvements and document issues with a “Final project report”.

Venue & Infrastructure contains the work done for contest preparation and security of it. The first part, Venue Selection begins with “Identifying venues” which helps to make a list of suitable places that meet the capacity and operation requirements. This is followed by “Site inspections” for confirming conditions as power, network and access. After decisioning, “Final venue contracting” takes place for applying infrastructure setup and preparation.

Infrastructure setup contains “Hall setup” to prepare the contest environment, “Network installation” for maintaining connectivity for contest platform, “Electricity & UPS setup” for stable supply of electricity and power, and “Lighting & cooling installation” for comfortable environment for participants and technical equipment.

Accommodation, Transport & Catering include all daily logistic operations that directly affect guests, participants. It includes “Hotel contracting” because accommodation capacity must be ensured beforehand for keeping the risk at the lowest level. Then “Room allocation for delegations” is done for planning rooms for teams and officials, “Shuttle route planning” for defining routes and scheduling between accommodation place and contest venue to make sure they arrive on time. Lastly, “Meal & catering services” is included since it must be planned in a controlled manner to ensure clear timing and coverage.

IT Systems & Contest Platform is one of the most critical pipelines because the entire contest relies on stable technical systems. It begins with System Development which includes “Server configuration” to prepare the core environment for hosting, “Contest system installation” to integrate contest platform into the environment, and “Registration portal development” for participant management and coordination.

Next, System Testing separated into different test stages as “Load testing” for verifying performance in peak usage periods, “Security penetration testing” to protect the event against security risks, and “Debugging & fixes” for final defects in the system.

Final deployment ensures the system’s functionality and durability. “Backup & failover setup” is included for recovering the system from any kind of failure, and “Final platform validation” for confirming the acceptability of the complete environment. Finally, “Competition Day readiness” ensures the final checks before the competition week.

Branding, media & sponsors milestone ensures that the event is promoted properly through sponsorships and announcements. The Branding part includes “Event visual identity” for setting visuals for the event to show on different platforms, “Website & social media updates” for maintaining ongoing communication with stakeholders, “Print & digital promotional materials” for considering official materials needed for promotion.

Media relations include “Press announcements” for maintaining official communication planned, “Media partner agreements” to maintain formal relationships with partners, and “Live event coverage planning” for smooth delivery of photos and videos captured during the event.

Sponsorship Management starts with “Identify potential sponsors” to define project targets, continues with “Sponsorship negotiations” for making agreements, and ends with “Finalize sponsorship agreements” to confirm sponsorships before the event delivery time.

Human Resources milestone includes the recruitment and training of volunteers and technical staff for the event. “Recruit translators” is also included because language support is essential for communication during the event. Furthermore, training includes “Security & medical briefing” for understanding safety procedures and emergency coordination before the event.

Contest Operations represent the preparations running during the event and includes “Pre-event test”, “Competition Week” execution, and “Post-event” wrap-up. Pre-event test includes setting up realistic testing conditions, simulate the event in those conditions and detect bugs, issues to fix them. That way the problems are addressed before the real event.

Competition week has a fixed date including opening/closing ceremonies, contest days and cultural events.

Post- event includes “Final cleanup” in which temporary setups are removed. Then, “Delegation departure coordination” for ensuring smooth leave of teams, and “Award distribution & media wrap-up” to distribute awards and complete remaining media activities.

Security & Medical Services ensure safety and operational protection during the event. Security part includes “Security planning” to define approach and responsibilities, “Venue security setup” for implementing physical security arrangements, and “Competition security teams” for providing security coverage. Medical part includes “On-site medical preparation” and “Emergency response readiness” to ensure services are available and can be executed immediately if needed. “Daily medical monitoring” helps to provide continuous health support.

2.2. WBS

ID	Task Name	Duration	Start Date	End Date	Predecessor	Cost	Resource Name
1	Project Management	742 days	Wed 12/20/23	Mon 10/19/26		\$76,448.00	
2	Project Initiation	248 days	Wed 12/20/23	Fri 11/29/24		\$7,824.00	
3	Obtain authorization	1 day	Wed 12/20/23	Wed 12/20/23		\$64.00	Project Manager
4	Confirm charter	10 days	Mon 11/4/24	Fri 11/15/24	3	(\$160.00)	PMO Coordinator
5	Form project team	10 days	Mon 11/18/24	Fri 11/29/24	4	\$7,920.00	Deputy Project Manager
6	Project Planning	242 days	Mon 2/3/25	Mon 1/5/26		\$31,440.00	

7	Stakeholder kick-off meeting	1 day	Mon 2/3/2 5	Mon 2/3/25	5	\$1,952.00	Project Manager
8	Approve budget planning	10 days	Mon 3/3/2 5	Fri 3/14/2 5	7	\$10,000.0 0	Finance Manager
9	Risk management plan	12 days	Mon 3/17/ 25	Tue 4/1/25	8	\$7,064.00	Project Manager
10	Winter meeting preparation	6 days	Mon 12/29 /25	Mon 1/5/26		\$10,360.0 0	Logistics Lead, Venue Coordinator
11	Conduct Winter meeting	1 day	Mon 1/5/2 6	Mon 1/5/26		\$2,064.00	Project Manager
12	Project Monitoring & Control	447 days	Tue 2/4/2 5	Mon 10/19/ 26		\$23,184.0 0	
13	Weekly status meetings	447 days	Tue 2/4/2 5	Mon 10/19/ 26	5	\$3,824.00	PMO Coordinator

14	Scope & timeline monitoring	434 days	Tue 2/4/2 5	Wed 9/30/2 6	5	\$26,624.0 0	Deputy Project Manager
15	Change & quality control	434 days	Tue 2/4/2 5	Wed 9/30/2 6	5	(\$7,264.00)	
16	Project Closing	18 days	Wed 9/9/2 6	Fri 10/2/2 6		\$14,000.0 0	
17	Final evaluation	5 days	Wed 9/9/2 6	Tue 9/15/2 6	75	\$5,000.00	Project Manager
18	Lessons learned	2 days	Wed 9/16/ 26	Thu 9/17/2 6	17	\$3,000.00	Project Manager
19	Final project report	10 days	Fri 9/18/ 26	Fri 10/2/2 6	18	\$6,000.00	Project Manager
20	Venue & Infrastructu re	429 days	Mon 4/21/ 25	Tue 8/18/2 6		\$952,488. 00	

21	Venue Selection	24 days	Mon 4/21/25	Thu 5/22/25		\$80,928.00	
22	Identify venues	10 days	Mon 4/21/25	Fri 5/2/25	8	\$400.00	Logistics Lead, Venue Coordinator
23	Site inspections	7 days	Mon 5/5/25	Tue 5/13/25	22	\$20,192.00	On-site Logistics Staff 1, Venue Coordinator
24	Final venue contracting	7 days	Wed 5/14/25	Thu 5/22/25	23	\$60,336.00	Contracts Officer, Finance Manager, Logistics Lead
25	Infrastructure Setup	61 days	Mon 9/15/25	Mon 12/8/25		\$239,520.00	
26	Hall setup	20 days	Mon 9/15/25	Fri 10/10/25	24	\$100,608.00	On-site Logistics Staff 1, Venue Coordinator
27	Network installation	15 days	Mon 10/13/25	Fri 10/31/25	26	\$60,480.00	Network Engineer, Network Technician 1, System Administrator

28	Electricity & UPS setup	10 days	Mon 11/3/ 25	Fri 11/14/ 25	27	\$39,840.0 0	Logistics Lead, On-site Logistics Staff 1
29	Lighting & cooling installation	16 days	Mon 11/17 /25	Mon 12/8/2 5	28	\$38,592.0 0	
30	Accommoda tion, Transport & Catering	143 days	Mon 2/2/2 6	Tue 8/18/2 6		\$632,040. 00	
31	Hotel contracting	9 days	Mon 2/2/2 6	Thu 2/12/2 6	24	\$200,856. 00	Accommodation Coordinator, Contracts Officer
32	Room allocation for delegations	10 days	Fri 2/13/ 26	Thu 2/26/2 6	31	\$50,240.0 0	Accommodation Coordinator, Protocol/Delegation Coordinator
33	Shuttle route planning	10 days	Fri 2/27/ 26	Thu 3/12/2 6	32	\$79,920.0 0	Transport Coordinator
34	Meal & catering services	33 days	Mon 7/6/2 6	Tue 8/18/2 6	31	\$301,024. 00	Catering Coordinator

35	IT Systems & Contest Platform	246 days	Mon 5/5/2 5	Fri 4/10/2 6		\$382,808. 00	
36	System Developmen t	51 days	Mon 5/5/2 5	Fri 7/11/2 5		\$213,872. 00	
37	Server configuration	15 days	Mon 5/5/2 5	Fri 5/23/2 5	9	\$80,672.0 0	IT Lead, Network Engineer, System Administrator
38	Contest system installation	16 days	Mon 5/26/ 25	Fri 6/13/2 5	37	\$61,440.0 0	Backend Developer, Frontend Developer, IT Lead
39	Registration portal development	20 days	Mon 6/16/ 25	Fri 7/11/2 5	38	\$71,760.0 0	Backend Developer, Frontend Developer, Registration Portal Developer
40	System Testing	32 days	Mon 7/14/ 25	Tue 8/26/2 5		\$101,816. 00	
41	Load testing	7 days	Mon 7/14/ 25	Tue 7/22/2 5	39	\$30,336.0 0	IT Lead, QA Engineer

42	Security penetration testing	10 days	Wed 7/23/ 25	Tue 8/5/25	41	\$40,880.0 0	Cybersecurity Specialist, IT Lead, QA Engineer
43	Debugging & fixes	15 days	Wed 8/6/2 5	Tue 8/26/2 5	42	\$30,600.0 0	Backend Developer, Frontend Developer
44	Final Deployment	30 days	Mon 3/2/2 6	Fri 4/10/2 6		\$67,120.0 0	
45	Backup & failover setup	10 days	Mon 3/2/2 6	Fri 3/13/2 6		\$41,680.0 0	IT Lead, Network Engineer, System Administrator
46	Final platform validation	5 days	Mon 3/16/ 26	Fri 3/20/2 6		\$9,720.00	
47	Competition- day readiness	15 days	Mon 3/23/ 26	Fri 4/10/2 6	46	\$15,720.0 0	Logistics Lead, Network Engineer, System Administrator
48	Branding, Media & Sponsors	75 days	Mon 6/2/2 5	Fri 9/12/2 5		\$251,056. 00	

49	Branding	45 days	Mon 6/2/2 5	Fri 8/1/25		\$149,680. 00	
50	Event visual identity	15 days	Mon 6/2/2 5	Fri 6/20/2 5	7	\$40,480.0 0	Graphic Designer, Media/PR Lead
51	Website & social media updates	10 days	Mon 6/23/ 25	Fri 7/4/25	50	\$39,520.0 0	Social Media Manager, Website Content Editor
52	Print & digital promotional materials	20 days	Mon 7/7/2 5	Fri 8/1/25	51	\$69,680.0 0	Registration Desk Staff
53	Media Relations	25 days	Mon 8/4/2 5	Fri 9/5/25		\$22,816.0 0	
54	Press announcements	5 days	Mon 8/4/2 5	Fri 8/8/25	52	\$1,000.00	Media Contact Person, Media/PR Lead
55	Media partner agreements	10 days	Mon 8/11/ 25	Fri 8/22/2 5	54	\$12,960.0 0	Finance Manager, Media Contact Person, Sponsorship Manager

56	Live event coverage planning	10 days	Mon 8/25/25	Fri 9/5/25	55	\$8,856.00	Photographer/Videographer
57	Sponsorship Management	75 days	Mon 6/2/25	Fri 9/12/25		\$78,560.00	
58	Identify potential sponsors	10 days	Mon 6/2/25	Fri 6/13/25	7	\$18,800.00	Finance Manager, Sponsorship Assistant, Sponsorship Manager
59	Sponsorship negotiations	15 days	Mon 6/16/25	Fri 7/4/25	58	\$40,000.00	Contracts Officer, Sponsorship Manager
60	Finalize sponsorship agreements	10 days	Mon 7/7/25	Fri 7/18/25	59	\$19,760.00	Contracts Officer, Social Media Manager
61	Human Resources	40 days	Mon 2/2/26	Fri 3/27/26		\$125,840.00	
62	Recruitment	30 days	Mon 2/2/26	Fri 3/13/26		\$66,280.00	

63	Recruit volunteers	20 days	Mon 2/2/2 6	Fri 2/27/2 6	7	\$35,640.0 0	General Volunteer Team, Volunteer Coordinator
64	Recruit technical staff	10 days	Mon 3/2/2 6	Fri 3/13/2 6	63	\$20,080.0 0	Project Manager
65	Recruit translators	10 days	Mon 3/2/2 6	Fri 3/13/2 6	63	\$10,560.0 0	Translation Lead, Translation Team
66	Training	10 days	Mon 3/16/ 26	Fri 3/27/2 6		\$59,560.0 0	
67	Volunteer orientation	4 days	Mon 3/16/ 26	Mon 3/23/2 6	63	\$20,160.0 0	General Volunteer Team, Volunteer Coordinator
68	Technical staff training	5 days	Mon 3/16/ 26	Fri 3/20/2 6	64	\$19,720.0 0	
69	Security & medical briefing	5 days	Mon 3/23/ 26	Fri 3/27/2 6	65,68	\$19,680.0 0	Medical Lead

70	Contest Operations	73 days	Mon 6/1/26	Tue 9/8/26		\$908,312.00	
71	Pre-Event Test	22 days	Mon 6/1/26	Tue 6/30/26		\$7,952.00	
72	Prepare test contest environment	10 days	Mon 6/1/26	Fri 6/12/26	46	\$3,040.00	QA Engineer, IT Lead, System Administrator
73	Run full-scale test event	2 days	Mon 6/15/26	Tue 6/16/26	72	\$2,032.00	Logistics Lead, On-site Logistics Staff 1, On-site Logistics Staff 2
74	Fix issues from test event	10 days	Wed 6/17/26	Tue 6/30/26	73	\$2,880.00	Backend Developer, Frontend Developer, QA Engineer
75	Competition Week	7 days	Sun 8/9/26	Sun 8/16/26		\$729,864.00	
76	Opening ceremony	1 day	Sun 8/9/26	Sun 8/9/26	74	\$119,928.00	

77	Contest Day 1	1 day	Wed 8/12/ 26	Wed 8/12/2 6	76	\$150,064. 00	Chief of Security, Medical Lead, Nurse Team 1, Protocol/Delegation Coordinator, Registration Desk Staff, Security Guards Team 1
78	Contest Day 2	1 day	Thu 8/13/ 26	Thu 8/13/2 6	77	\$150,088. 00	Chief of Security, Medical Lead, Protocol/Delegation Coordinator, Registration Portal Developer, Security Guards Team 2, Nurse Team 1
79	Cultural events	2 days	Mon 8/10/ 26	Tue 8/11/2 6		\$219,856. 00	Ceremony Support Volunteer Team 2
80	Closing ceremony	1 day	Sun 8/16/ 26	Sun 8/16/2 6		\$89,928.0 0	

81	Post-Event	17 days	Mon 8/17/ 26	Tue 9/8/26		\$170,496. 00	
82	Final cleanup	5 days	Mon 8/17/ 26	Fri 8/21/2 6	80	\$30,160.0 0	Logistics Support Volunteer Team, On-site Logistics Staff 1, On-site Logistics Staff 2
83	Delegation departure coordination	6 days	Mon 8/24/ 26	Mon 8/31/2 6	82	\$40,096.0 0	Registration Desk Staff, Transport Coordinator
84	Award distribution & media wrap-up	6 days	Mon 8/17/ 26	Mon 8/24/2 6		\$100,240. 00	Accountant, Photographer/Videogra pher, Finance Manager
85	Security & Medical Services	48 days	Mon 6/15/ 26	Tue 8/18/2 6		\$120,376. 00	
86	Security	47 days	Mon 6/15/ 26	Mon 8/17/2 6		\$60,192.0 0	

87	Security planning	6 days	Mon 6/15/ 26	Sun 6/21/2 6	28	\$14,904.0 0	
88	Venue security setup	30 days	Mon 6/22/ 26	Fri 7/31/2 6	87	\$20,240.0 0	Security Guards Team 3
89	Competition security teams	6 days	Mon 8/10/ 26	Mon 8/17/2 6	88	\$25,048.0 0	Security Guards Team 3
90	Medical	13 days	Mon 8/3/2 6	Tue 8/18/2 6		\$60,184.0 0	
91	On-site medical preparation	5 days	Mon 8/3/2 6	Fri 8/7/26	28	\$20,080.0 0	Medical Lead, Nurse Team 1
92	Emergency response readiness	5 days	Mon 8/10/ 26	Fri 8/14/2 6	91	\$15,160.0 0	Doctor, Emergency Nurse Team
93	Daily medical monitoring	7 days	Mon 8/10/ 26	Tue 8/18/2 6		\$24,944.0 0	Nurse Team 2

3. Project Budget

3.1. Explanation of Budget Table

The project budget was developed with the bottom-up estimation in Microsoft Project. For each task, there is one or more assigned resources from the Resource Sheet. According to it, task costs were calculated automatically by Microsoft Project from resource hourly rates and task duration.

3.2. Resource Sheet

A Resource Sheet was created to show the roles during IOI 2026 event. Roles from different categories separated to improve accountability. They are separated based on management, finance, IT, logistics, media, sponsorships, HR, volunteers, security and medical. Since, each task is assigned to a role, broad resource names helped us to prevent resource allocation problem. All resources are defined as “Work” with a maximum unit of 100%, cost accrual set to Prorated, and overtime rates are set to \$0.

3.3. Uzbekistan Calendar

A separate calendar for Uzbekistan was created and assigned to project resources. This helps to schedule tasks considering non-working days. The calendar includes standard non-working weekends. Additionally, national holidays entered as exceptions for years 2023-2026:

- New Year Holiday
- Novruz Holiday
- Eid al-Fitr Holiday
- Remembrance Day
- Eid al-Adha Holiday

- Independence Day

- Teachers' Day

- Constitution Day

3.4. Project Budget Table

Task Name	Fixed Cost
Project Management	\$76,448.00
Project Initiation	\$7,824.00
Obtain authorization	\$64.00
Confirm charter	(\$160.00)
Form project team	\$7,920.00
Project Planning	\$31,440.00
Stakeholder kick-off meeting	\$1,952.00
Approve budget planning	\$10,000.00
Risk management plan	\$7,064.00
Winter meeting preparation	\$10,360.00
Conduct Winter meeting	\$2,064.00
Project Monitoring & Control	\$23,184.00
Weekly status meetings	\$3,824.00
Scope & timeline monitoring	\$26,624.00
Change & quality control	(\$7,264.00)
Project Closing	\$14,000.00
Final evaluation	\$5,000.00
Lessons learned	\$3,000.00

Final project report	\$6,000.00
Venue & Infrastructure	\$952,488.00
Venue Selection	\$80,928.00
Identify venues	\$400.00
Site inspections	\$20,192.00
Final venue contracting	\$60,336.00
Infrastructure Setup	\$239,520.00
Hall setup	\$100,608.00
Network installation	\$60,480.00
Electricity & UPS setup	\$39,840.00
Lighting & cooling installation	\$38,592.00
Accommodation, Transport & Catering	\$632,040.00
Hotel contracting	\$200,856.00
Room allocation for delegations	\$50,240.00
Shuttle route planning	\$79,920.00
Meal & catering services	\$301,024.00
IT Systems & Contest Platform	\$382,808.00
System Development	\$213,872.00
Server configuration	\$80,672.00
Contest system installation	\$61,440.00
Registration portal development	\$71,760.00
System Testing	\$101,816.00

Load testing	\$30,336.00
Security penetration testing	\$40,880.00
Debugging & fixes	\$30,600.00
Final Deployment	\$67,120.00
Backup & failover setup	\$41,680.00
Final platform validation	\$9,720.00
Competition-day readiness	\$15,720.00
Branding, Media & Sponsors	\$251,056.00
Branding	\$149,680.00
Event visual identity	\$40,480.00
Website & social media updates	\$39,520.00
Print & digital promotional materials	\$69,680.00
Media Relations	\$22,816.00
Press announcements	\$1,000.00
Media partner agreements	\$12,960.00
Live event coverage planning	\$8,856.00
Sponsorship Management	\$78,560.00
Identify potential sponsors	\$18,800.00
Sponsorship negotiations	\$40,000.00
Finalize sponsorship agreements	\$19,760.00
Human Resources	\$125,840.00
Recruitment	\$66,280.00
Recruit volunteers	\$35,640.00

Recruit technical staff	\$20,080.00
Recruit translators	\$10,560.00
Training	\$59,560.00
Volunteer orientation	\$20,160.00
Technical staff training	\$19,720.00
Security & medical briefing	\$19,680.00
Contest Operations	\$908,312.00
Pre-Event Test	\$7,952.00
Prepare test contest environment	\$3,040.00
Run full-scale test event	\$2,032.00
Fix issues from test event	\$2,880.00
Competition Week	\$729,864.00
Opening ceremony	\$119,928.00
Contest Day 1	\$150,064.00
Contest Day 2	\$150,088.00
Cultural events	\$219,856.00
Closing ceremony	\$89,928.00
Post-Event	\$170,496.00
Final cleanup	\$30,160.00
Delegation departure coordination	\$40,096.00
Award distribution & media wrap-up	\$100,240.00
Security & Medical Services	\$120,376.00
Security	\$60,192.00

Security planning	\$14,904.00
Venue security setup	\$20,240.00
Competition security teams	\$25,048.00
Medical	\$60,184.00
On-site medical preparation	\$20,080.00
Emergency response readiness	\$15,160.00
Daily medical monitoring	\$24,944.00


4. Gantt Chart

4.1. Explanation of Gantt Chart and Critical Path

The Gantt chart represents the whole project life cycle which includes initiation, planning, execution, closing and the delivery of the project to the competition. It also emphasizes the parallel work streams such as preparation of venue and infrastructure, development of IT platform, branding, sponsorship, and planning of human resources. All the activities are congruent to the fixed dates of the week of competition. The timetable is more intensive during the event preparation phase between June and August 2026. During this phase, the team concentrates on pre-event testing, resolve final issues, and contest day preparation.

Activities whose slack was equal to zero were seen as critical ones. Any delay in such activities would directly influence the project completion date. The critical path of this project plan primarily contains the activities that are concerned with infrastructure readiness, final platform validation and competition readiness, preset competition testing, fixing of issues, and the deterministic order of the activities in the competition week.

4.2. Visualization

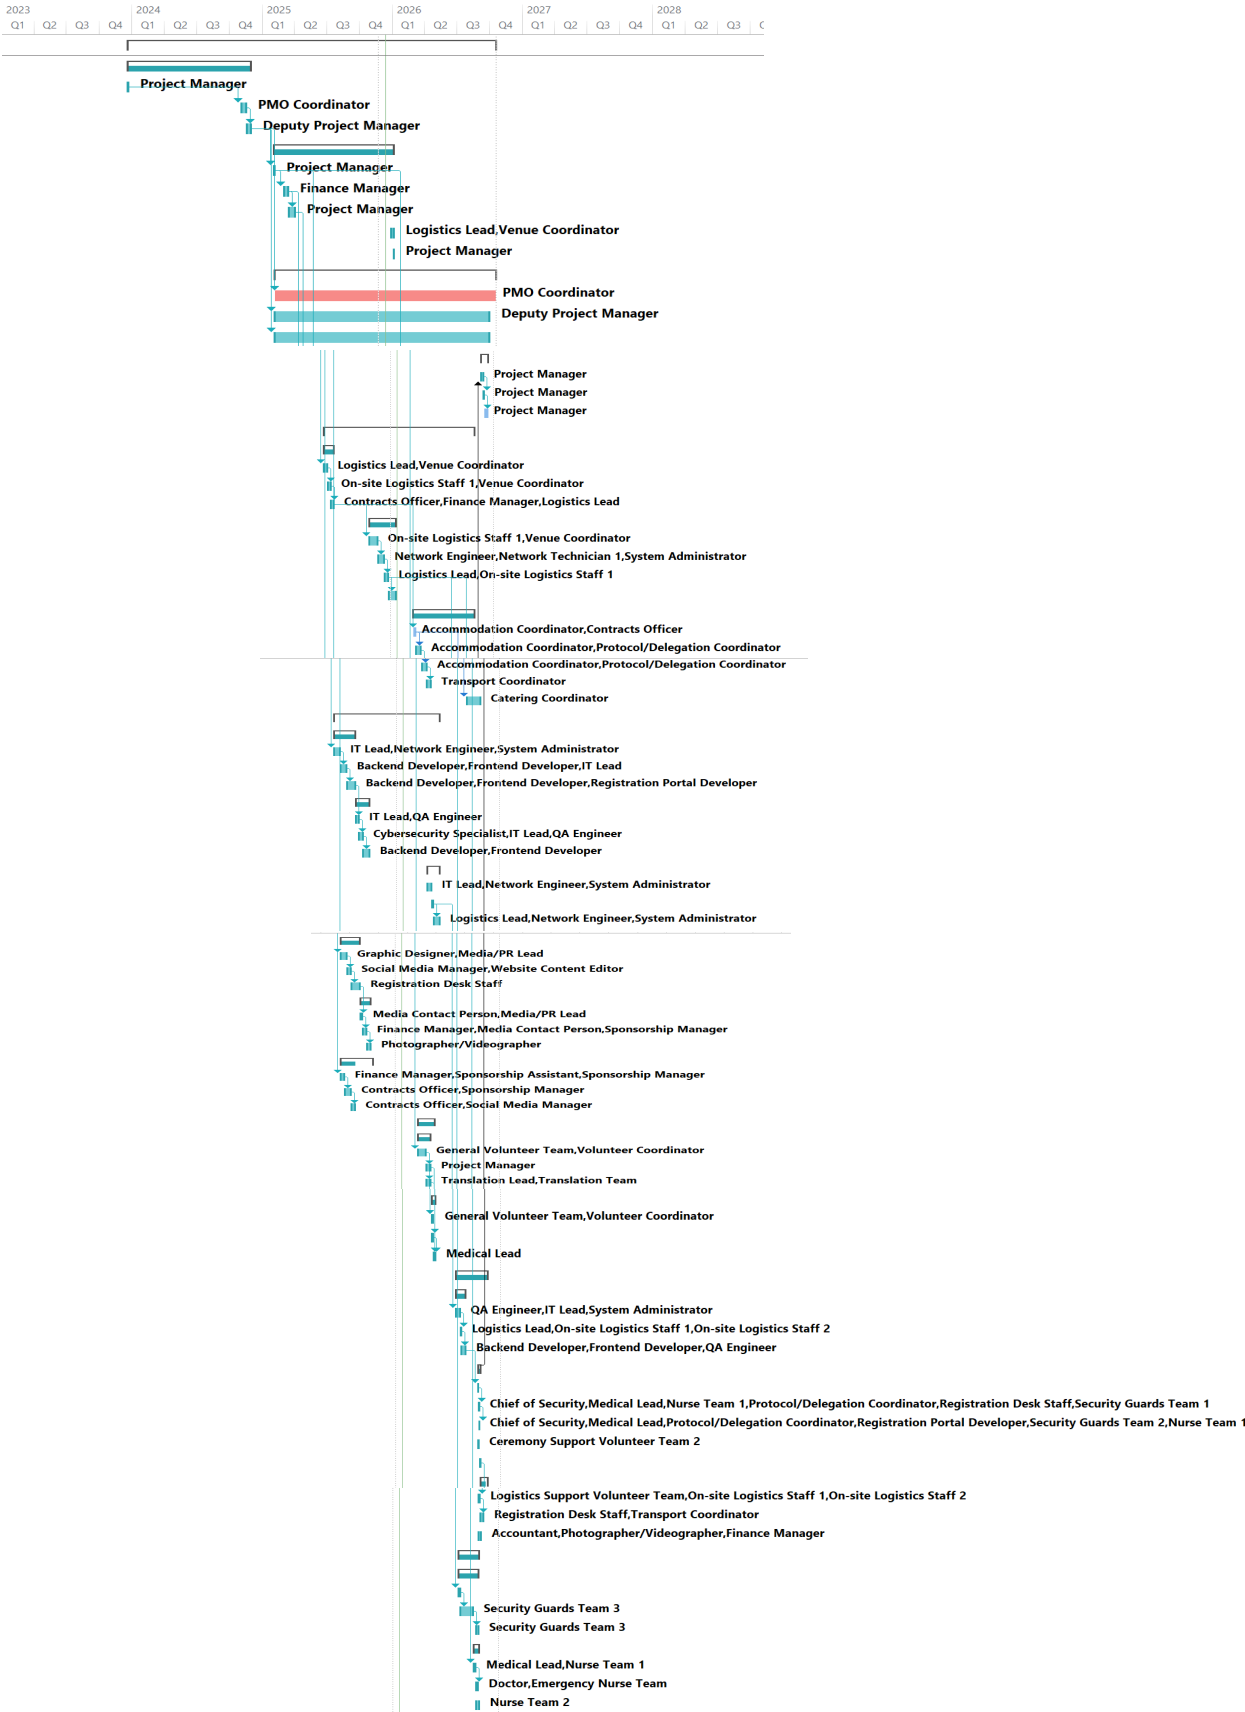

References

(n.d.). Retrieved from <https://www.timeanddate.com/holidays/uzbekistan/2023>

(2025). Retrieved from IOI 2026 Website: <https://ioi2026.uz/>

Individual Contribution Table

Team Member	Contribution to the event and report	Estimated %
Ulkar Ahmadli	Developed project schedule, budget and completed report	%50
Javid Ibadov	Developed project schedule, budget and completed report	%50
Raul Hatamov		%0
